

Early Milestones

- March 2013 Consultative committee created
 - Composed of members of the Finance Council, Pastoral Advisory Council,
 School Board, & others appointed by the Pastor
 - Oversee overall management of the parish property
 - Identify how Ma Ke Kula could meet the needs of Parish/School
 - Determine if Ma Ke Kula is needed to meet future needs
 - If needed, how to fund the property & any future improvements
- April & May 2013 How to proceed?
 - Reviewed 2010 Leeward Vicariate demographic study
 - Identified a lack of Parish headcounts since October 2010
 - Identify possible future facilities to meet the mission of OLPH
 - Parish Center, Preschool, Ministry offices/classrooms?
 - Realization sets in



The Master Plan

- July October 2013 Request for qualifications released
 - 11 Consultants/architects 4 responses
 - Review proposals, conduct interviews & reference checks
 - Selection of Saavedra Gehlhausen Architects
- Demographic update
 - SGA collaborates with Helber Hastert & Fee Planners
 - Developer review of homes built 2010-2014
 - Concludes the addition of 350 new parishioners by 2036
 - Reviewed updated mass headcounts
 - Largest typical mass & Christmas mass overflows
 - Determines minimum church size of 700 seats
- Existing site & facility analysis
 - Review zoning & planning requirements



The Master Plan (Continued)

- Suitability & condition of existing structures for renovation/expansion
- Site utilities water, sewer & electric
- Suitability of Ma Ke Kula for uses other than residential
- Church, Office, & School Structurally Sound Relative To Age, But......
 - None Meet Current International Building Codes
 - Fire Suppression Systems
 - ADA Requirements
 - HVAC Systems In Church & Office
 - Nearing End Of Useful Life
 - Do Not Meet Current Ventilation Codes
 - Church & Office Roofs Need Replacement
 - Water & Electrical Service Inadequate For Renovation Or Expansion
 - Church Doors/Windows Need Repair
 - Parking/Paving In Poor Condition
 - No Site Drainage
 - Restroom Fixtures In Poor Condition
 - Expansion Would Require Additional Fixtures To Meet Code



The Master Plan (Continued)

- Space planning
 - A 91% increase of square footage to meet all needs through 2036
 - Can be accommodated on existing campus
 - It is determined that there is no good development path to expand into Ma
 Ke Kula
 - Removal of residential infrastructure would be cost prohibitive
- Developed 11 options consolidated down to 4 plus the status quo
 - Options presented to ministries & parishioners
 - Selected option broken down into 3 phases
 - Phase I Construct new church & renovate existing restrooms

The Financial Challenge

- Regardless Of The Option Selected Construction Cost Is \$7.9 \$8.4 Million For Phase 1
- Ma Ke Kula Debt Is \$2.5 Million
 - 5-year interest only
 - Assessed Value \$5.1 Million
- OLPH's Capital Campaign Pledge Capability
 - \$2.0-\$3.0 Million
- Financial Capability Questionable

Sale of Ma Ke Kula & Capital Campaign

- December 2015-January 2016 Engage CCS to develop a capital campaign
 - \$3 million goal 5 years
 - Begins in April 2016
- We appeal to the Bishop after months of unsuccessfully seeking financing alternatives to allow the sale of Ma Ke Kula
 - Permission to market the property is received
 - CBRE is engaged to market Ma Ke Kula
- Ma Ke Kula is listed for \$5.7 million
 - Broker's opinion of value is \$5.2 million
- September 2016 Ma Ke Kula closes at \$5.3 million


Project Management & Architectural Design Services

- December 2016 Engaged Rider Levett Bucknall to act as Project Manager
 - Develop Request for Proposal
- March 2017 RFP released to 6 pre-vetted architectural firms for design services
 - Receive 4 responses
 - Conduct bid analysis & interviews
- December 2017 Domus Studio selected to provide design services
 - November 2018 Conceptual Design includes Conditional Use Permit
 - February 2019 Schematic Design Phase
 - April 2019 Design Development Phase
 - Construction Documents Phase includes permitting, pre-construction, construction & post construction services




Construction Documents Phase

- May 2020 Release RFP to 8 pre-vetted GC's
 - Conduct site visits, interviews & reference checks
- July 2020 Select Design Build Hawaii
 - Pre-construction services "Design Assist"
- June 2021 PSRF construction loan approved
 - Permanent financing TBD
- July 2021 Construction Documents submitted to DPP & 3rd
 Party Reviewer
 - And now we wait

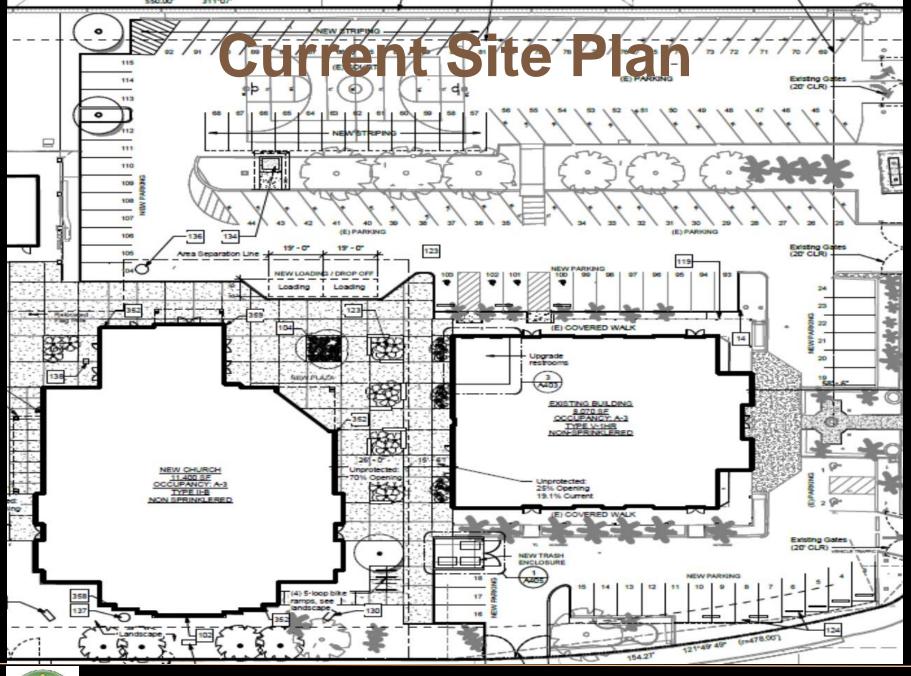



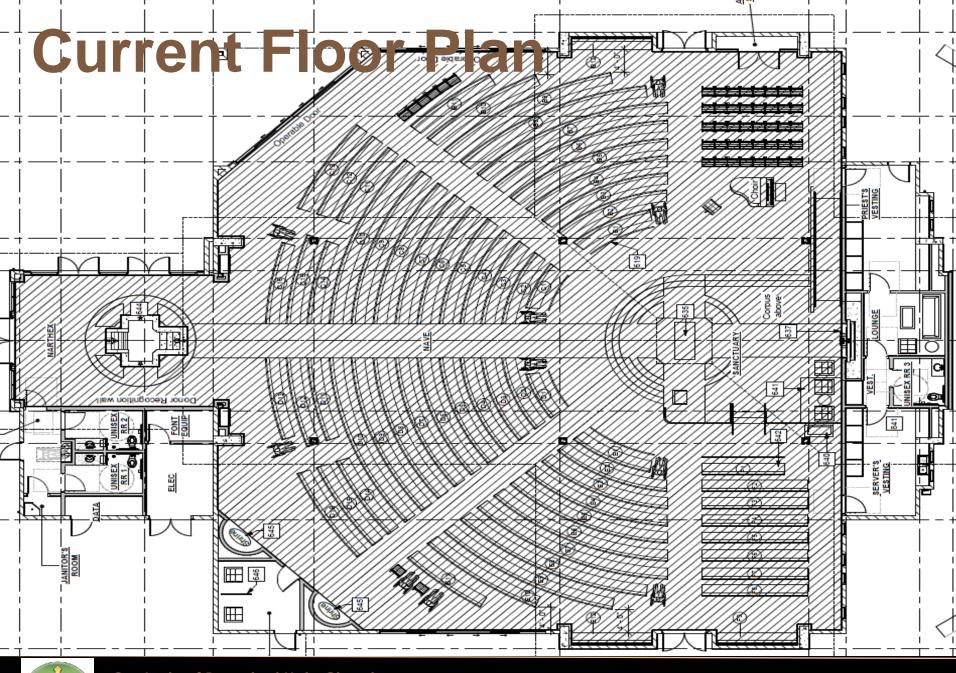

Next Steps

- Secure permits & commence construction-???
- August 2021 Donor Opportunities
 - Seek donors for liturgical furnishings
- September 2021 Finalize construction contract
 - All subcontractor pricing locked in
- Application for permanent financing TBD

Project Cost

Development Cost

Design & Engineering	1,274,106
Permitting	85,000
Construction +	7,973,836
FF&E	468,169
Project Management	376,471
Financial, Taxes, Legal	127,250
Contingency	1,000,000

Total Cost 11,304,832

HCCF

Beginning Balance

Pledge Redemptions** 2,817,699

Interest Inc on HCCF

Less: Project Cost 2,817,699

Ending Balance

Building Fund

Bldg Fund (Beg)

Mahele Na Makana***

Lease Rent/School Facilities****

Donor Opportunities****

526,191

Interest Inc on Bldg Fund

20,913

Less: Project Cost

3,744,666

Bldg Fund (End)*

Construction Loan (Beg)

Loan Draws 4,695,767
Interest Exp on Loan 46,700



Questions

